


I1

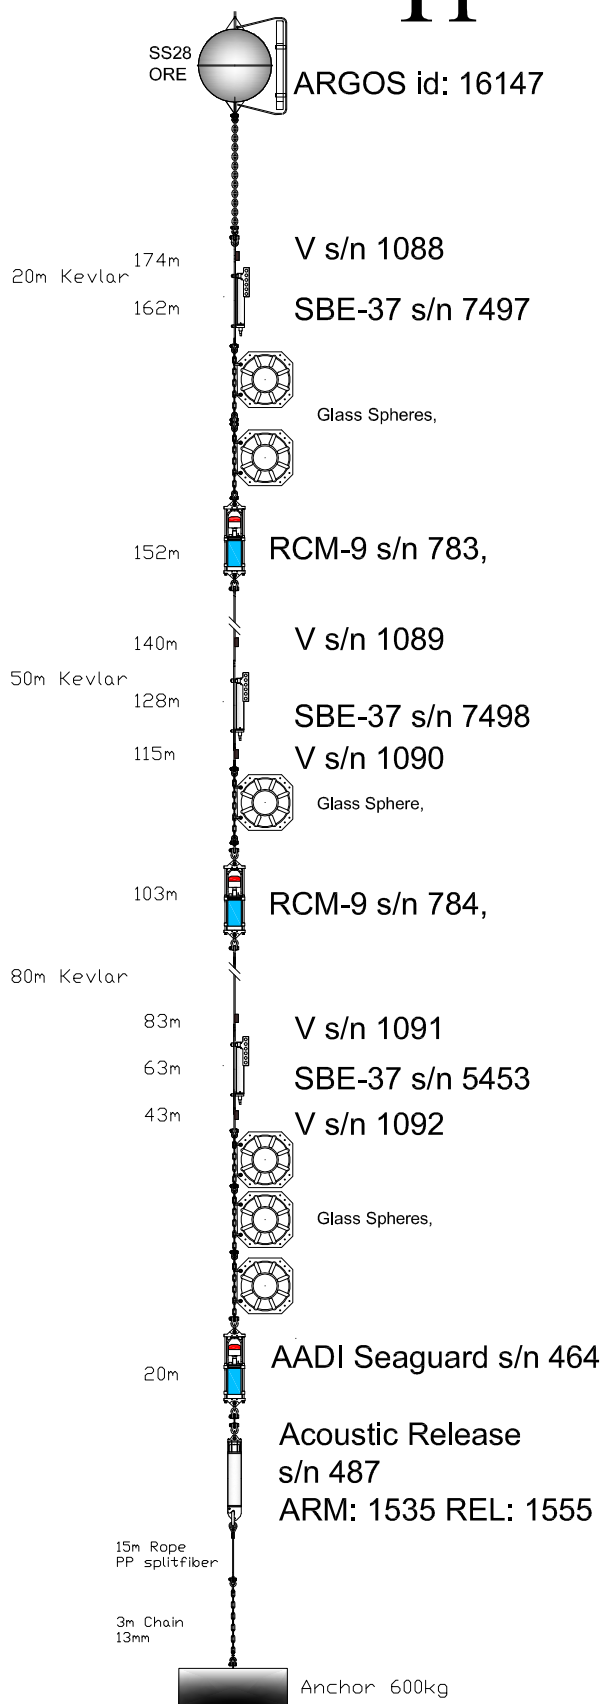

UNIS

Project: Isfjorden 2012
 Location: I1
 Position: N78 03.643 E 013 31.327
 Depth: 202m
 Deployment: 06.09.2012 Time 14:28
 Recover: _____
 Comments: _____

Instruments	
2	AADI RCM-9 in Frame
1	AADI Seaguard in Frame
3	SBE-37
5	Vemco, term
1	Acoustic Release Oceano
1	ARGOS - SMM 500

Mooring Floatation	
1	Steel Buoy m/ argosbracket
6	VITROVEX 432mm Glass Spheres, Buoyancy 260 N

Mooring Line	
20m	11mm Kevlar Line
50m	11mm Kevlar Line
80m	11mm Kevlar Line
15m	Rope Polypropylen 20mm 6m
0.8m	Chain 13mm steel galvanic
1.6m	Chain 13mm steel galvanic
5m	Chain 20mm steel galvanic
3m	Chain 13mm steel galvanic

Mooring Hardware	
1	Thimble 20mm steel galvanic (for rope splice)
1	Thimble 20mm (POM GI) (for rope splice)
1	Anchor Steel 600kg wet weight
12	Shackle Red pin 1,5 t (pin 13mm)
10	Shackle Red pin 2 t (pin 16mm)
10	Shackle Red pin 3.25 t (pin 19mm)
1	S10 "Frekhaug" stainless steel (329), ring for release
